



SITE INVESTIGATION FACTUAL REPORT

Report No: SI-930113
Client: Sedgwick International UK - Maidstone
Site: 2 Main Street, Ratby
Leicestershire
Client Ref: 10420891
Date of Visit: 4/12/2024



Home Emergency Response - Subsidence Investigation - Drainage Services – Crack & Level Monitoring – Property Video Surveys

East Building, Cable Drive, Walsall, WS2 7BN


☎ 0333 016 4477

✉ siinstructions@cet-uk.com

🌐 www.cet-uk.com

CET is the trading name of CET Structures Ltd


Registered in England No. 02527130

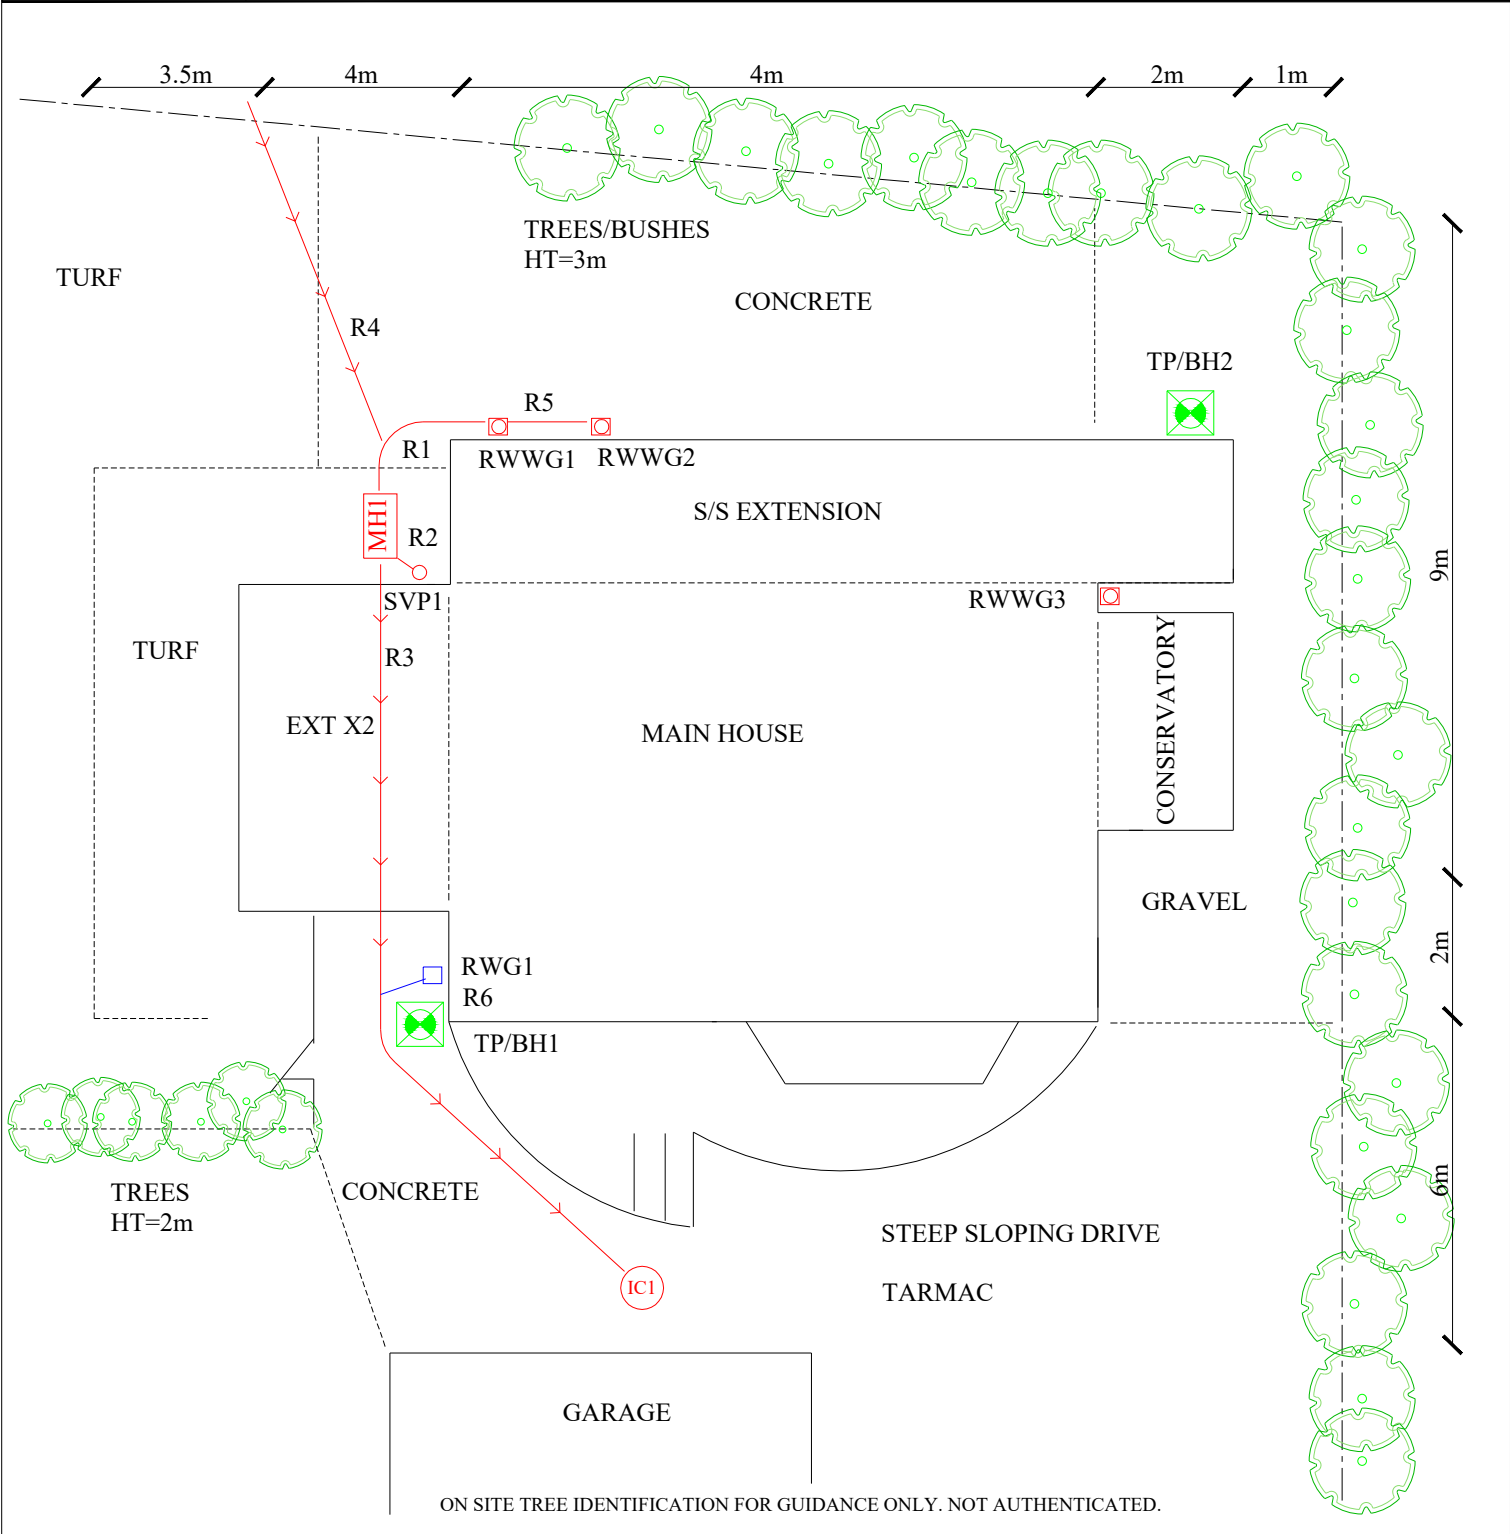

Remarks:	Key:		Surface Water Drain	---
	Combined Gulley	RWWG	Foul Water Drain	---
Scale: N.T.S.	Manhole	MH	Tree / Bush	(approx. ht in m)
	Rain Water Pipe	RWP		
	Rain Water Gulley	RWG	Trial Pit	
	Soil Vent Pipe	SVP	Borehole	
	Waste Gulley	WG	O/D - Open Discharge	
	Waste Pipe	WP		

REPORT NUMBER: C5005560 / 325027.1.1.1
TRIAL PIT REF: TP1
CLIENT: Sedgwick International UK
JOB NO: 930113
EXCAVATION METHOD: Hand tools

DATE: 04/12/2024
SITE: 2 MAIN STREET
WEATHER: Dry

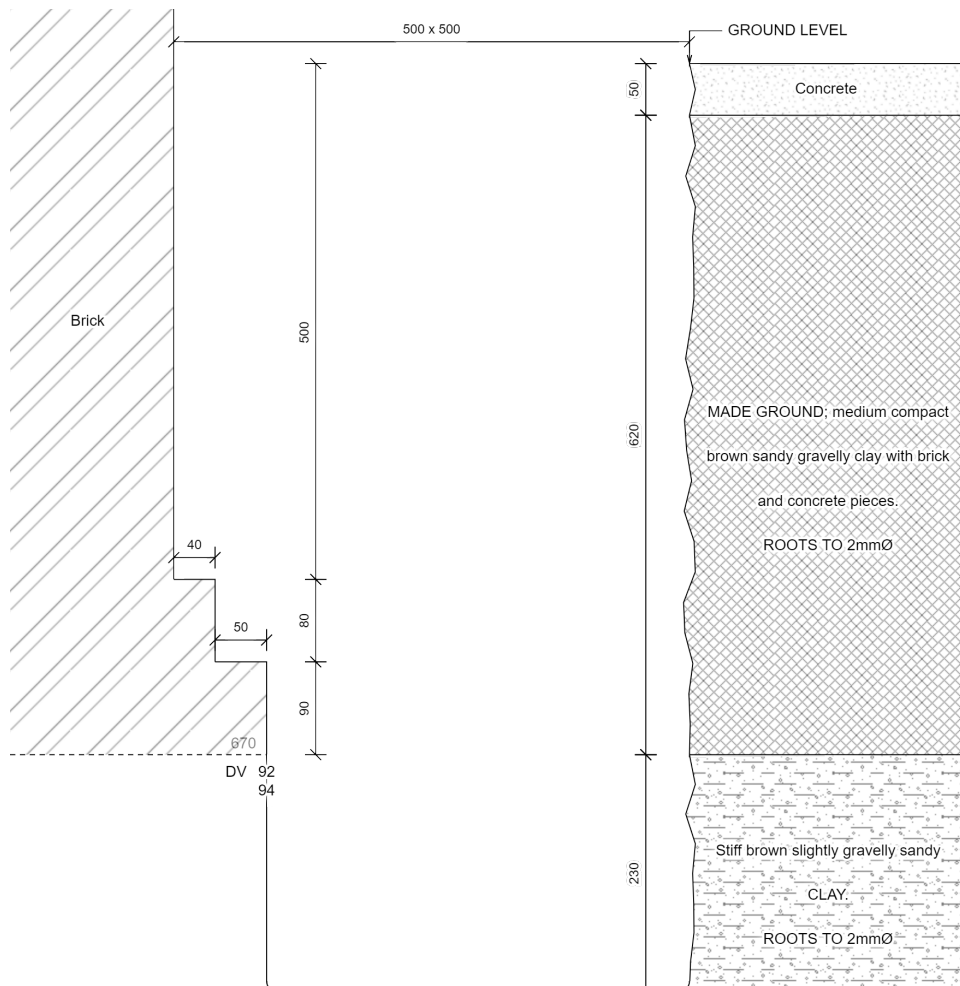

For Strata below 900mm see Bore Hole log

curved steel pin driven 200mm under foundation at 670mm below ground level.

Key:
D Small disturbed sample J Jar sample
B Bulk disturbed sample V Pilcon vane (kPa)
W Water sample M Mackintosh probe
TDTD Too dense to drive

Remarks:
Test results reported relate only to the items tested.
This report shall not be reproduced except in full without approval of the Laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

For and on behalf of CTS
Cara Kosma - Project Delivery Supervisor


Cara Kosma

Approved Signatory
Report date 05-Dec-24

Borehole		1		Sheet:	1 of 1	Site:	2 MAIN STREET				
				Job No:	930113						
				Date:	04/12/2024						
Boring Method:		Hand Auger		Ground Level:		Client:	SEDGWICK INTERNATIONAL UK				
Diameter (mm):		75	Weather:		dry						
Depth	Soil Description					Thickness	Legend	Samples and Tests			
(m)								Depth	Type	Result	
0.00	See Trial Pit					0.90					
0.90	Stiff brown slightly gravelly sandy CLAY					0.50		1.00	DV	130+	
										130+	
1.40	Medium dense to dense brown slightly gravelly SAND					0.30		1.50	DM	50(20)	
		50(10)									
1.70	End of BH										
Remarks: BH ends at 1.7m too dense to hand auger. A second BH was attempted within the TP with similar results not logged, BH dry and open on completion.						Key: D - Disturbed Sample B - Bulk Sample W - Water Sample Roots J - Jar Sample Roots V - Pilcon Shear Vane (kPa) Roots M - Mackintosh Probe Depth to Water (m) TDTD - Too Dense To Drive				To	Max
										Depth	Dia
										(m)	(mm)
										1.40	1
Logged: PB		CK	Checked:	Approved:	Version V1.0 28/01/16		N.T.S.				

REPORT NUMBER: C5005560 / 325027.1.1.2
TRIAL PIT REF: TP2
CLIENT: Sedgwick International UK
JOB NO: 930113
EXCAVATION METHOD: Hand tools

DATE: 04/12/2024
SITE: 2 MAIN STREET
WEATHER: Dry

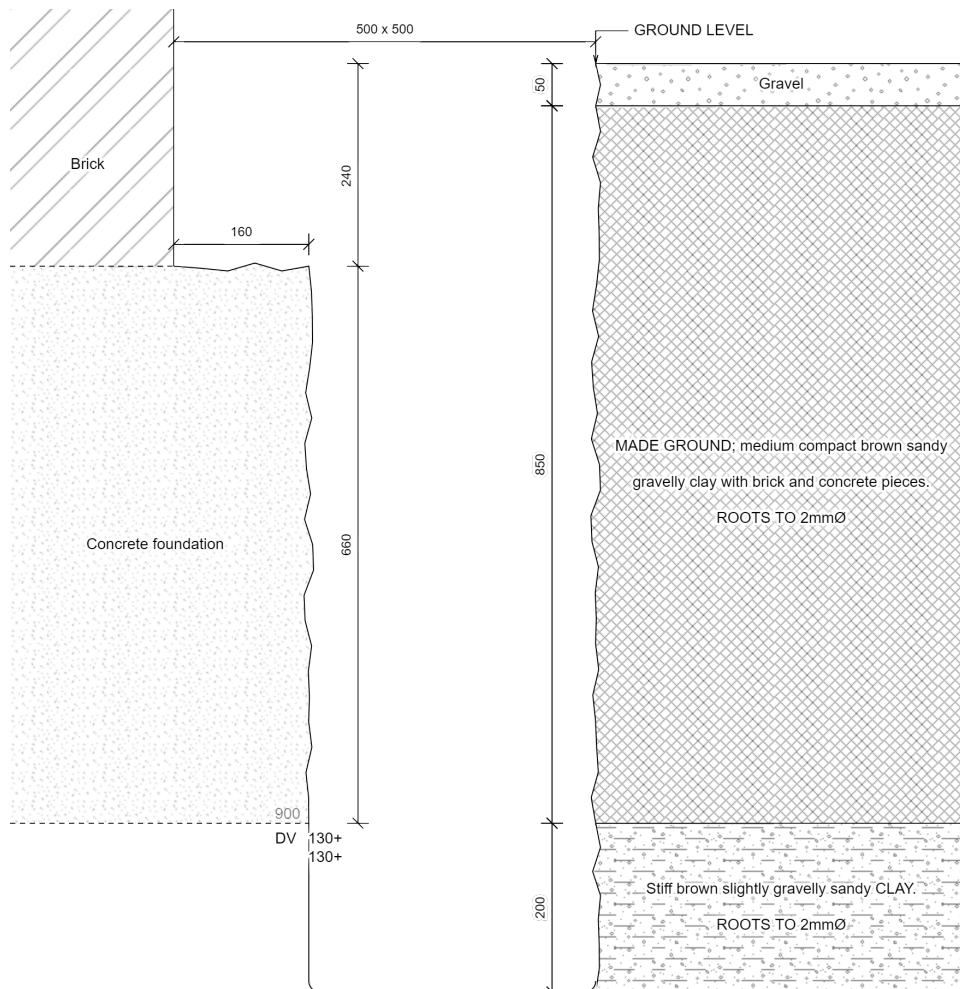

For Strata below 1100mm see Bore Hole log

Curved steel pin driven 200mm under foundation at 900mm below ground level.

Key:
D Small disturbed sample J Jar sample
B Bulk disturbed sample V Pilcon vane (kPa)
W Water sample M Mackintosh probe
TDTD Too dense to drive

Remarks:
Test results reported relate only to the items tested.
This report shall not be reproduced except in full without approval of the Laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

For and on behalf of CTS
Cara Kosma - Project Delivery Supervisor

Cara Kosma

Approved Signatory
Report date 05-Dec-24

Borehole		2		Sheet:	1 of 1	Site:	2 MAIN STREET										
				Job No:	930113												
				Date:	04/12/2024												
Boring Method:		Hand Auger		Ground Level:		Client:	Sedgwick International UK										
Diameter (mm):		75	Weather:		dry												
Depth	Soil Description								Samples and Tests								
(m)							Thickness	Legend	Depth	Type	Result						
0.00	See Trial Pit						1.10										
1.10	Stiff brown sandy gravelly CLAY						0.20										
1.30	Medium dense to dense brown slightly gravelly silty SAND						0.40										
									1.50	DM	50(10)						
											50(5)						
1.70	End of BH										TDTD						
Remarks: BH ends at 1.7m too dense to hand auger. A second BH was attempted within the TP with similar results not logged, BH dry and open on completion.						Key: D - Disturbed Sample B - Bulk Sample W - Water Sample Roots J - Jar Sample Roots V - Pilcon Shear Vane (kPa) Roots M - Mackintosh Probe Depth to Water (m) TDTD - Too Dense To Drive											
Logged: PB		CK	Checked:		Approved:	Version V1.0 28/01/16		N.T.S.									

SITE INVESTIGATION LABORATORY TEST REPORT

SI REPORT NUMBER: 930113

CLIENT : CET Property Assurance (Sedgwick International UK)

SITE:
2 Main Street
Ratby
Leicester
LE6 0JG

DATE OF SITE VISIT:
04/12/2024

DATE RECEIVED BY LABORATORY:
04/12/2024

Approved by : 
C Kosma - Project Delivery Supervisor

DATE REPORTED: 11-Dec-2024

The testing on this report has been subcontracted, see Summary for testing
Laboratory details

Our Ref :930113

Location :2 Main Street

Client:CET Property Assurance (Sedgwick International UK)

Address:CET, Unit 4, Boundary Court, Willow Farm Business Park, Castle Donington, DE74 2NN

Laboratory Summary Results

Date Sampled:04/12/2024

Date Received :04/12/2024

Date Tested :10/12/2024

Date of Report :11/12/2024

Sample Ref		Type	# Moisture Content	# Soil Fraction > 0.425mm	# Liquid Limit	# Plastic Limit	~ Plasticity Index	~ Liquidity Index	~ Modified Plasticity Index	~ Soil Class	# Filter Paper Contact Time	# Soil Sample Suction	# Oedometer Strain	~ Estimated Heave Potential	In situ Shear Vane Strength	Organic Content	pH Value	Sulphate Content		* Class
TP/BH No	Depth (m)																	SO3 (g/l)	SO4 (mg/l)	
			(%) [1]	(%) [2]	(%) [3]	(%) [4]	(%) [5]	[5]	(%) [6]	[7]	(d)	(kPa) [8]	[9]	(mm) [10]	(kPa) [11]	(%) [12]	[13]	[14]	[15]	[16]
1	U/S 0.67	D	23	8	55	22	33	0.04	30	CH					93					
	1.0	D	20	6	50	21	29	-0.05	27	CH					> 130					
	1.5	D	17	10	ENP - SAND															

Test Methods / Notes

[1] BS 1377 - Part 2 : 2022 : Clause 4

[2] Estimated if <5%, otherwise measured

[3] BS 1377 - Part 2 : 2022 : Clause 5

[4] BS 1377 - Part 2 : 2022 : Clause 6

[5] BS 1377 - Part 2 : 2022 : Clause 6

[6] BRE Digest 240 : 1993

[7] BS 5930 : 2018 : Figure 8 - Plasticity Chart for the classification of fines soils

[8] Building Research Establishment Information Paper 4/93

[9] In Accordance with BS 1377-5 : 1990 : Clause 3

[10] Estimated Heave Potential (Dd)

[11] Values of shear strength were determined in situ by CTS using a Pilcon hand vane or Geonor vane (GV).

[12] BS 1377 : Part 3 : 2018 + A1 2021 Clause 4 - Tested By CTS Leicester

[13] BS 1377 : Part 3 : 2018 + A1 2021 Clause 12 - Tested By CTS Leicester

[14] Sulphate content as SO3 as required by BS 1377: Part 3: 1990 has been provided for information purposes - Tested By CTS Leicester

[15] BS 1377 : Part 3 : 2018 + A1 2021 Clause 7.6 - Tested By CTS Leicester

[16] BRE Special Digest One (Concrete in Aggressive Ground) August 2005

Note that if the SO4 content falls into the DS-4 or DS-5 class, it would be prudent to consider the sample as falling into the DS-4M or DS-5M class respectively unless water soluble magnesium testing is undertaken to prove otherwise.

PSD Chart - BS 1377: Part 2 : 1990, Test No 9.2

~ Calculations performed using subcontracted data.

* These tests are not UKAS accredited

Key

D Disturbed sample (small)

B Disturbed sample (bulk)

U Undisturbed sample

W Groundwater sample

ENP Essentially Non-Plastic by inspection

U/S Underside of Foundation

Test results reported relate only to the items tested.

This report shall not be reproduced except in full without approval of the laboratory.

The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Opinions and interpretations expressed herein are outside of the scope of UKAS accreditation.

These tests have been subcontracted and carried out by PSL (Part of the Phenna Group)

Full reports can be provided upon request.


Address: CET, Unit 4, Boundary Court, Willow Farm Business Park, Castle Donington, DE74 2NN

Date of Report : 11/12/2024

Version: BH V1 SUBCON - 28.03.2023

Moisture Content Profiles

Our Ref : 930113
Location : 2 Main Street
Work carried out for: CET Property Assurance (Sedgwick International UK)

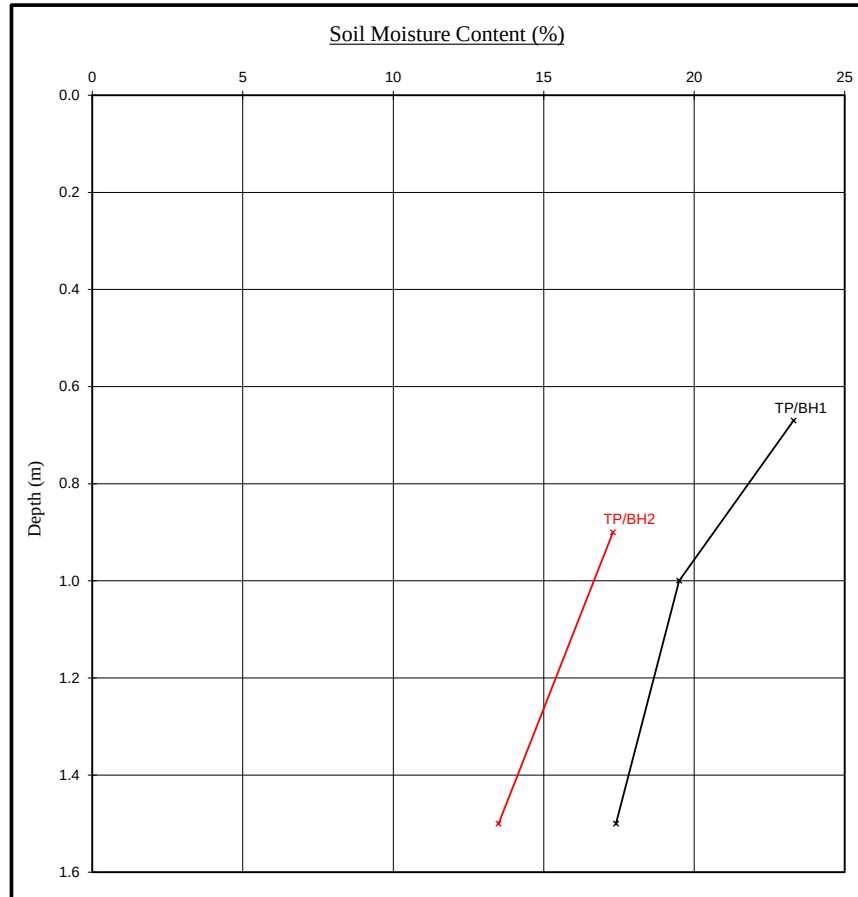


Notes

1. If plotted, 0.4 LL and PL+2 (after Driscoll, 1983) should only be applied to London Clay (and similarly overconsolidated clay) at shallow depths.
2. Unless specifically noted the profiles have not been related to a site datum.

Shear Strength Profiles

Date Sampled : 04/12/2024
Date Received : 04/12/2024
Date Tested : 10/12/2024
Date of Report : 11/12/2024

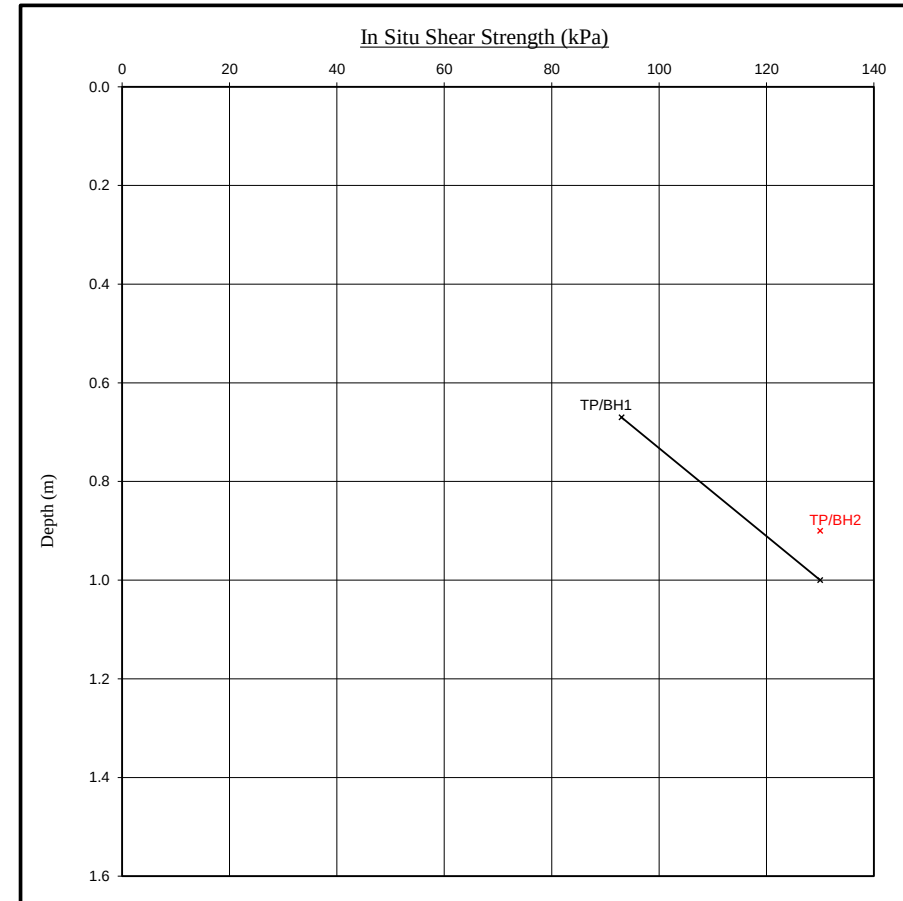

Note

1. Unless otherwise stated, values of Shear Strength were determined in situ by CTS using a Pilcon Hand Vane the calibration of which is limited to a maximum reading of 130 kPa.
2. Unless specifically noted the profiles have not been related to a site datum.

Construction Testing Solutions
4 Oak Spinney Park
Ratby Lane
Leicester Forest East
Leicestershire
LE3 3AW

Intec
Parc Menai, Bangor,
Gwynedd, North Wales
LL57 4FG
Tel: 01248 672652
Fax: 01248 672601

ROOT IDENTIFICATION

2 Main Street

Client Reference: 930113
Report Date: 6 December 2024
Our Ref: R59471

Sub Sample	Species Identified		Root Diameter	Starch
TP1:				
USF	<i>Hedera</i> or <i>Fatsia</i> spp.	1	7 mm	Abundant
BH1:				
to 1.4m	Pomoideae gp.	2	1 mm	Absent
TP2:				
USF	Pomoideae gp.	3	2 mm	Abundant
BH2:				
to 1.7m	Pomoideae gp.	4	2 mm	Abundant

Comments:

- 1 - Plus 3 others the same.
- 2 - Plus 3 others also identified as Pomoideae gp. All in a state of decay.
- 3 - Plus 3 others also identified as Pomoideae gp.
- 4 - Plus 1 other also identified as Pomoideae gp.

Hedera spp. include ivy; *Fatsia* spp. are shrubs closely related to ivy.

Pomoideae gp include apple, cotoneaster, hawthorn, pear, pyracantha, quince, rowan, snowy mespil and whitebeam.

Signed: R. Shaw

Unless we are otherwise instructed in writing, the above sample material will normally be disposed of 6 years after the date of this report.



Manhole Details	Sheet:	1 of 1	Site:	2 MAIN STREET
	Job No.:	930113		
	Date:	04/12/24	Client:	SEDGWICK INTERNATIONAL UK

MH:- MH1 Depth:- 400 (mm)

Depths of run if
different to invert level:-

Manhole Condition:-

Chamber Dimension:-

600

 /

450

 (mm)

Depths of run if
different to invert level:-

Manhole Condition:-

Chamber Dimension:- / (mm)

Depths of run if
different to invert level:-

Manhole Condition:-

Chamber Dimension:- / (mm)

Interceptor



Internal Back Drop.

External Back Drop.

Coding Sheet		Sheet:		Site:	2 MAIN STREET				
		Job No.:	930113						
		Date:	04/12/2024	Client:	SEDGWICK INTERNATIONAL UK				

Run:	1									
From:	MH2		Invert Level:	400		Direction:	U/S			
To:	U/S		Invert Level:			Function:	Comb			
Pipe Material:	PVC		Pipe Dia:	100						
Water/Pressure Test:			Drain Break-In:	No		Gully Condition:	As Built			
Distance (m)	Code	Clock Ref at to	Dia mm	Intrusion % mm		Shared Run:	No			
						If Shared How:				
0.00	ST						Surface Material	Length (m)		
0.40	JN	10				Junction at	concrete			
0.70	LR					Line deviates right				
2.10	FH					rwwg1 reached				
Comments:										

Run:	2									
From:	MH1		Invert Level:	400		Direction:	U/S			
To:	U/S		Invert Level:			Function:	Comb			
Pipe Material:	PVC		Pipe Dia:	100						
Water/Pressure Test:			Drain Break-In:	No		Gully Condition:				
Distance (m)	Code	Clock Ref at to	Dia mm	Intrusion % mm		Shared Run:	No			
						If Shared How:				
0.00	ST					Remarks	Surface Material	Length (m)		
0.40	LU				90	Line deviates up	concrete			
0.70	FH					sv p1 reached				
Comments:										

Run:	3											
From:			MH2		Invert Level:		400		Direction:		D/S	
To:			D/S		Invert Level:				Function:		Comb	
Pipe Material:			PVC		Pipe Dia:		100					
Water/Pressure Test:					Drain Break-In:		No		Gully Condition:			
Distance (m)	Code	Clock Ref at to		Dia mm	Intrusion % mm		Shared Run:		Yes			
							If Shared How:		Off boundary			
0.00	ST						Remarks		Surface Material		Length (m)	
1.00	JN	10					Junction at		under building			
1.50	MC						vc					
4.70	JDM						Joint displaced medium					
7.70	RMJ				10		Roots mass					
8.30	JN	11					Junction at					
9.80	LL						Line deviates left					
10.40	JDM						Joint displaced medium					
11.80	MC						pvc					
11.80	LR						Line deviates right					
12.60	FH						ic1 reached					
Comments:												

Run:	4											
From:			jn		Invert Level:		400		Direction:		U/S	
To:			U/S		Invert Level:				Function:		Comb	
Pipe Material:			PVC		Pipe Dia:		100					
Water/Pressure Test:					Drain Break-In:		Yes		Gully Condition:			
Distance (m)	Code	Clock Ref at to		Dia mm	Intrusion % mm		Shared Run:		Yes			
							If Shared How:		Off boundary			
0.00	ST						Remarks		Surface Material		Length (m)	
5.00	FH						passed rear boundary		concrete			
Comments:												

Run:	5											
From:			rwwg1		Invert Level:		200		Direction:		U/S	
To:			rwwg2		Invert Level:				Function:		F/W	
Pipe Material:					Pipe Dia:		100					
Water/Pressure Test:					Drain Break-In:		No		Gully Condition:		As Built	
Distance (m)	Code	Clock Ref at to		Dia mm	Intrusion % mm		Shared Run:					
							If Shared How:					
0.00	ST						Remarks		Surface Material		Length (m)	
1.20	LU						Line deviates up		concrete			
1.50	FH						rwwg2 reached					
Comments:												

Run:	6									
From:			jn	Invert Level:		400	Direction:		U/S	
To:			U/S	Invert Level:			Function:		Comb	
Pipe Material:			VC	Pipe Dia:		100				
Water/Pressure Test:				Drain Break-In:		No	Gully Condition:			
Distance (m)	Code	Clock Ref at to		Dia mm	Intrusion % mm		Shared Run:		No	
							If Shared How:			
0.00	ST						Remarks		Surface Material	Length (m)
0.50	JDL						Joint displaced large		concrete	
0.60	FH						rwg1 reached			
Comments:										

To: Sedgwick International
Subsidence Scanning Centre
Ground Floor
Fountain Court
West Yorkshire
LS27 0JG

Our Ref: **930113**

Your Ref: **0**

Date: **5-Dec-24**

Ftiao: 0

ESTIMATE

Site:- 2 Main Street

Item		Amount
1.0	Location	JN U/S - Run 6
	Shared System	No
	Condition Grade	B
	Drain Serviceability	Unserviceable
	Work Spec	Excavate and replace gully and pipe work to run 3

Manhole & run's 3 and 4 at the left of the property are shared, therefore owned by the water authority. Repairs may be the responsibility of the water authority.

Notes

Repairs to shared runs and off boundary pipe-work may be the responsibility of the water authority.

Total £503.58

Condition Grade

A - Structurally sound with no leakage evident.

B - Cracks and fractures observed.

C - Structurally unsound

plus VAT @20% £100.72

Total + VAT £604.30

Quotation is binding only if accepted within 28 days from date of issue and is subject to our Standard Terms and Conditions
The price qualification notes, stated on the drainage solutions schedule of rates, apply to this quotation.
CET Structures Ltd undertakes to return to site free of charge to carry out remedial work to the drainage repairs set out above for a period of 2 months from the date of this invoice. The company standard charge rates will apply to the visit should the work requested be unrelated to the said repairs.

ESTIMATING & COSTING SHEET - DOMESTIC DRAINAGE

Site:- 2 Main Street

Client :- Sedgwick International

Attention of:-

Client ref	
Job Number :-	930113
Insurer	
Date:-	5-Dec-24
Recommendation	1

Item No	Description JN U/S - Run 6	Unit	Quantity	Rate (£)	Price (£)
1.0	Emergency Drain Blockage Clearance				
1.1	Unblock drain 8am-6pm - First 1/2 Hour	Item		£76.30	£0.00
1.2	Unblock drain 8am-6pm- Subsequent 1/2 Hour	Item		£32.70	£0.00
1.3	Unblock drain 6pm-midnight	Item		£109.00	£0.00
1.4	Unblock drain 6pm-midnight - Subsequent 1/2 hour	Item		£38.15	£0.00
2.1	CCTV Surveys				
2.2	Undertake CCTV survey 8am-6pm (up to 3 hours)	Item		£141.70	£0.00
2.3	Additional 1/2 hr survey charge	Item		£32.70	£0.00
3.0	Replacing Underground Drainage				
3.1	Gullies				
3.2	Take out and replace gully (100mm outlet)	Item	1	£141.70	£141.70
3.3	Take out and replace rodding point (100mm outlet)	Item		£98.10	£0.00
3.4	Bends/junctions				
3.5	Excavate and replace rest bend (100mm outlet)	Item		£98.10	£0.00
3.6	Excavate and replace rest bend (150mm outlet)	Item		£130.80	£0.00
3.7	Excavate and replace junction/bend (100mmØ), Excavation depth 0-1m.	Item	2	£76.30	£152.60
3.8	Excavate and replace junction/bend (150mmØ), Excavation depth 0-1m	Item		£76.30	£0.00
3.9	Excavate and replace junction/bend (100mmØ), Excavation depth 1-1.5m.	Item		£76.30	£0.00
3.10	Excavate and replace junction/bend (150mmØ), Excavation depth 1-1.5m.	Item		£76.30	£0.00
3.11	Excavate and replace junction/bend (100mmØ), Excavation depth 1.5-2.0m.	Item		£76.30	£0.00
3.12	Excavate and replace junction/bend (150mmØ), Excavation depth 1.5-2.0m.	Item		£76.30	£0.00
3.13	Pipes				
3.14	Excavate trench and replace 100mmØ pipework, Excavation depth 0-1m, First 10m.	m	1	£103.55	£103.55
3.15	Excavate trench and replace 150mmØ pipework, Excavation depth 0-1m, First 10m.	m		£130.80	£0.00
3.16	Excavate trench and replace 100mmØ pipework, Excavation depth 0-1m.	m		£103.55	£0.00
3.17	Excavate trench and replace 150mmØ pipework, Excavation depth 0-1m.	m		£130.80	£0.00
3.18	Excavate trench and replace 100mmØ pipework, Excavation depth 1-1.5m, First 10m.	m		£163.50	£0.00
3.19	Excavate trench and replace 150mmØ pipework, Excavation depth 1-1.5m, First 10m.	m		£174.40	£0.00
3.20	Excavate trench and replace 100mmØ pipework, Excavation depth 1-1.5m.	m		£163.50	£0.00
3.21	Excavate trench and replace 150mmØ pipework, Excavation depth 1-1.5m.	m		£174.40	£0.00
3.22	Excavate trench and replace 100mmØ pipework, Excavation depth 1.5-2.0m, First 10m.	m		£294.30	£0.00
3.23	Excavate trench and replace 150mmØ pipework, Excavation depth 1.5-2.0m, First 10m.	m		£316.10	£0.00
3.24	Excavate trench and replace 100mmØ pipework, Excavation depth 1.5-2.0m.	m		£272.50	£0.00
3.25	Excavate trench and replace 150mmØ pipework, Excavation depth 1.5-2.0m.	m		£294.30	£0.00
3.26	Surface Reinstatement of Trenches				
3.27	Excavate through and reinstate turf.			£0.00	£0.00
3.28	Excavate through and replace concrete paving slabs	m		£32.70	£0.00
3.29	Excavate through and replace block paving	m		£54.50	£0.00
3.30	Excavate through and reinstate plain concrete, maximum thickness 100mm.	m	1	£51.23	£51.23
3.31	Excavate through and reinstate plain concrete, thickness 100- 200mm.	m		£103.55	£0.00
3.32	Excavate through and reinstate reinforced concrete, maximum thickness 100mm.	m		£98.10	£0.00
3.33	Excavate through and reinstate reinforced concrete, thickness 100-200mm.	m		£125.35	£0.00
3.34	Excavate through and reinstate Tarmac - Cold rolled	m		£52.32	£0.00
3.35	Excavate through and reinstate Tarmac - Hot rolled	m		POA	
3.36	Reinstatement of crazy paving	m		£81.75	£0.00
4.0	Lining				
4.1	Set up lining rig for drain lining including first 3m of lining per run, for 100mm or 150mm	Item		£316.10	£0.00
4.2	Line 100mmØ drain	m		£54.50	£0.00
	Super Flex Liner 100mm drain	m		£98.10	£0.00
4.3	Line 150mmØ drain	m		£76.30	£0.00
	Super Flex Liner 150mm drain	m		£119.90	£0.00
4.4	Post lining CCTV survey	no		£109.00	£0.00
4.5	Minimum lining charge	Item		£316.10	£0.00
4.6	Root cutting of drain prior to lining	hr		£70.85	£0.00
4.7	Set up lining rig for patch lining	Item		£0.00	£0.00
4.8	Patch line 100mmØ drain	no		£272.50	£0.00
4.9	Patch line 150mmØ drain	no		£305.20	£0.00
4.10	Post patch lining CCTV survey	Item		£109.00	£0.00
4.11	Minimum patch lining charge	Item		£272.50	£0.00
4.12	Re-open lateral branch up to 2m length, pipe up to 150mm	no		£207.10	£0.00
4.13	Re-open lateral branch over 2m length, pipe up to 150mm	no		£305.20	£0.00
	Epoxy resin	no		£23.98	£0.00
5.0	Miscellaneous				
5.1	Excavation and backfill of soakaway (1m3) with stone	Item		£436.00	£0.00
5.2	% Uplift on disbursements and suppliers charges	%		1.36	£0.00
5.3	Daywork - Hourly labour rate	hr		£32.70	£0.00
5.4	Minimum project value	Item		£377.69	£0.00
5.5					£0.00
5.6					£0.00
5.7					£0.00
5.8					£0.00
6.0	Additional items				
6.1	De-scaling (fat/grime)	hr		£70.85	£0.00
6.2	De-scaling (scale using chain flails)	hr		£98.10	£0.00
6.3	Gully surround	item	1	£32.70	£32.70
6.4	Manhole works (up to 1.2m)	item		£87.20	£0.00
6.6	Oversize soakaway (1.5m3)	item		£654.00	£0.00
6.7	Soakaway >1.5m3	item		POA	
6.8	Waste disposal	m	1	£21.80	£21.80
6.9	Shoring	m		£43.60	£0.00
	Total Estimate Price For Recommendation Number		1.0		£503.58
	Subject to discount			0.00	£0.00
	Total subject to VAT @ 20%				£503.58

Note: Subject to the attached Terms and Conditions

A - When calculating prices, all measurements are rounded up

C - Every effort will be made to match existing surfaces where disturbed although this cannot be guaranteed

G - Daywork rates do not include for materials that are charged at cost plus 25%

KEY: ne = not exceeding, eo = extra over rate, m = linear metre, nr = number, hr = hour

B - Depths are taken to the base of excavations

D - All rates exclude VAT

F - The above rates are subject to re-measurement

E - Depths are taken to the base of excavations

CET STRUCTURES LTD TERMS AND CONDITIONS

Site:- 2 Main Street

Client :- Sedgwick International

Attention of:-

Client Ref:-

Job Number:- 930113

Insurer:-

Date:- 5-Dec-24

General Terms and Conditions

- 1 On site parking is a prerequisite of any drain repair contract. This quotation is to the addressee only and should not be forwarded unless prior agreement is obtained from CET Structures Ltd. Every effort will be made to match existing surfaces however, there will be evidence of excavation works in certain circumstances.
- 2 The rates do not include for excavation of surfaces other than soft ground or concrete < 100mm thick; reinstatement other than concrete <100mm thick; internal excavations; reinstatement >750mm in width; excavation of depths greater than 1.2m; reinforced concrete.
- 3 CET's standard soakaway that is priced on the agreed alliance schedule of drainage rates is constructed to dimensions specified in the NHBC Guidelines for small soakaways. The soakaway is generally located 5m from any foundations (should site constraints permit) and is constructed to provide adequate short term surface water storage and percolation into surrounding ground. This small 1m³ soakaway is usually of sufficient capacity to accommodate average rainfall from an average surface area of roof space, however in extreme weather conditions and /or larger than average roof surface area feeding the soakaway, surcharging may occur. Alternative designs and prices are available at a cost along with percolation testing. Certain ground conditions may not be suitable for soakaway design due to low permeability and this information is not always readily available.

Notes

For excavation and reinstatement of any steps, will be done on day work rate.

With a minimum of 4 hours. Materials at cost plus 25%.

Any obstacles, shrubs & plants that are located in the working area will need to be removed by others to allow for these works

Water Authority Sewer Condition Codes

B	Broken pipe at... (or from... to..) o'clock	JN	Junction at...o'clock, diameter...mm
BR	Branch Major	JX	Junction defective at.. o'clock, diameter.. mm
CC	Crack circumferential from... to... o'clock	LC	Lining of sewer changes/starts/finishes at this
CL	Crack longitudinal @... o'clock	LD	Line of sewer deviates down
CM	Cracks multiple from... to... o'clock	LL	Line of sewer deviates left
CN	Connection at... o'clock, diameter... mm	LN	Line defect at (or from.. to..) o'clock
CNI	Connection at... o'clock, diameter... mm, intrusion... mm	LR	Line of sewer deviates right
CU	Camera under water	LU	Line of sewer deviates up
CX	Connection defective at... o'clock	MB	Missing bricks at.. (or from.. to..) o'clock
CXI	Connection defective at... o'clock, diameter... mm, intrusion... mm	MC	Material of sewer changes at this point
D	Deformed sewer... %	MH	Manhole/node
DB	Displaced bricks at (or from.. to..) o'clock	MM	Mortar missing medium at.. (or from.. to..) o'clock
DC	Dimension of sewer changes at this point	MS	Mortar missing surface at.. (or from.. to..) o'clock
DE	Debris (non silt/grease)... % cross-sectional loss	MT	Mortar missing total at.. (or from.. to..) o'clock
DEG	Debris grease... % cross-sectional area loss	OB	Obstruction... % height/diameter loss
DES	Debris silt... % cross-sectional area loss	OJL	Open joint large
DI	Dropped invert, gap... mm	OJM	Open joint medium
EHJ	Encrustation heavy from.. to.. o'clock % cross-sectional area loss (at joint)	PC	Length of pipe forming sewer changes at this new length...mm
ELJ	Encrustation light from.. to.. o'clock%	RFJ	Roots fine (at joint)
EMJ	Encrustation medium from.. to.. o'clock %, cross-sectional area loss (at joint)	RMJ	Roots mass... % cross-sectional area loss (at joint)
ESH	Scale heavy... % cross-sectional area loss from... to... o'clock	RTJ	Roots tap (at joint)
ESL	Scale light from... to... o'clock	SA	Survey abandoned
ESM	Scale medium... % cross-sectional area loss from... to... o'clock	SC	Shape of sewer changes at this point
FC	Fracture circumferential from... to... o'clock	SSL	Surface damage, spalling large at (or from.. to..) o'clock
FL	Fracture longitudinal at... o'clock	SSM	Surface damage, spalling medium at (or from.. to..) o'clock
FM	Fractures multiple from... to... o'clock	SSS	Surface damage, spalling slight at (or from.. to..) o'clock
GO	General observation at this point	SWL	Surface damage, wear large at... (or from.. to..) o'clock
GP	General photograph number... taken at this point	SWM	Surface damage, wear medium at... (or from.. to..) o'clock
H	Hole in sewer at... o'clock	SWS	Surface damage, wear slight at.. (or from.. to..) o'clock
IDJ	Infiltration dripper at (or from... to...) o'clock (at joint)	V	Vermin (rats and mice)
IGJ	Infiltration gusher at (or from... to...) o'clock (at joint)	WL	Water level... % height/diameter
IRJ	Infiltration runner at (or from... to...) o'clock (at joint)	X	Sewer collapsed... % cross-sectional area loss
ISJ	Infiltration seep at (or from... to...) o'clock (at joint)	FH	End of survey
JDM	Joint displaced medium		
JDL	Joint displaced large		
