


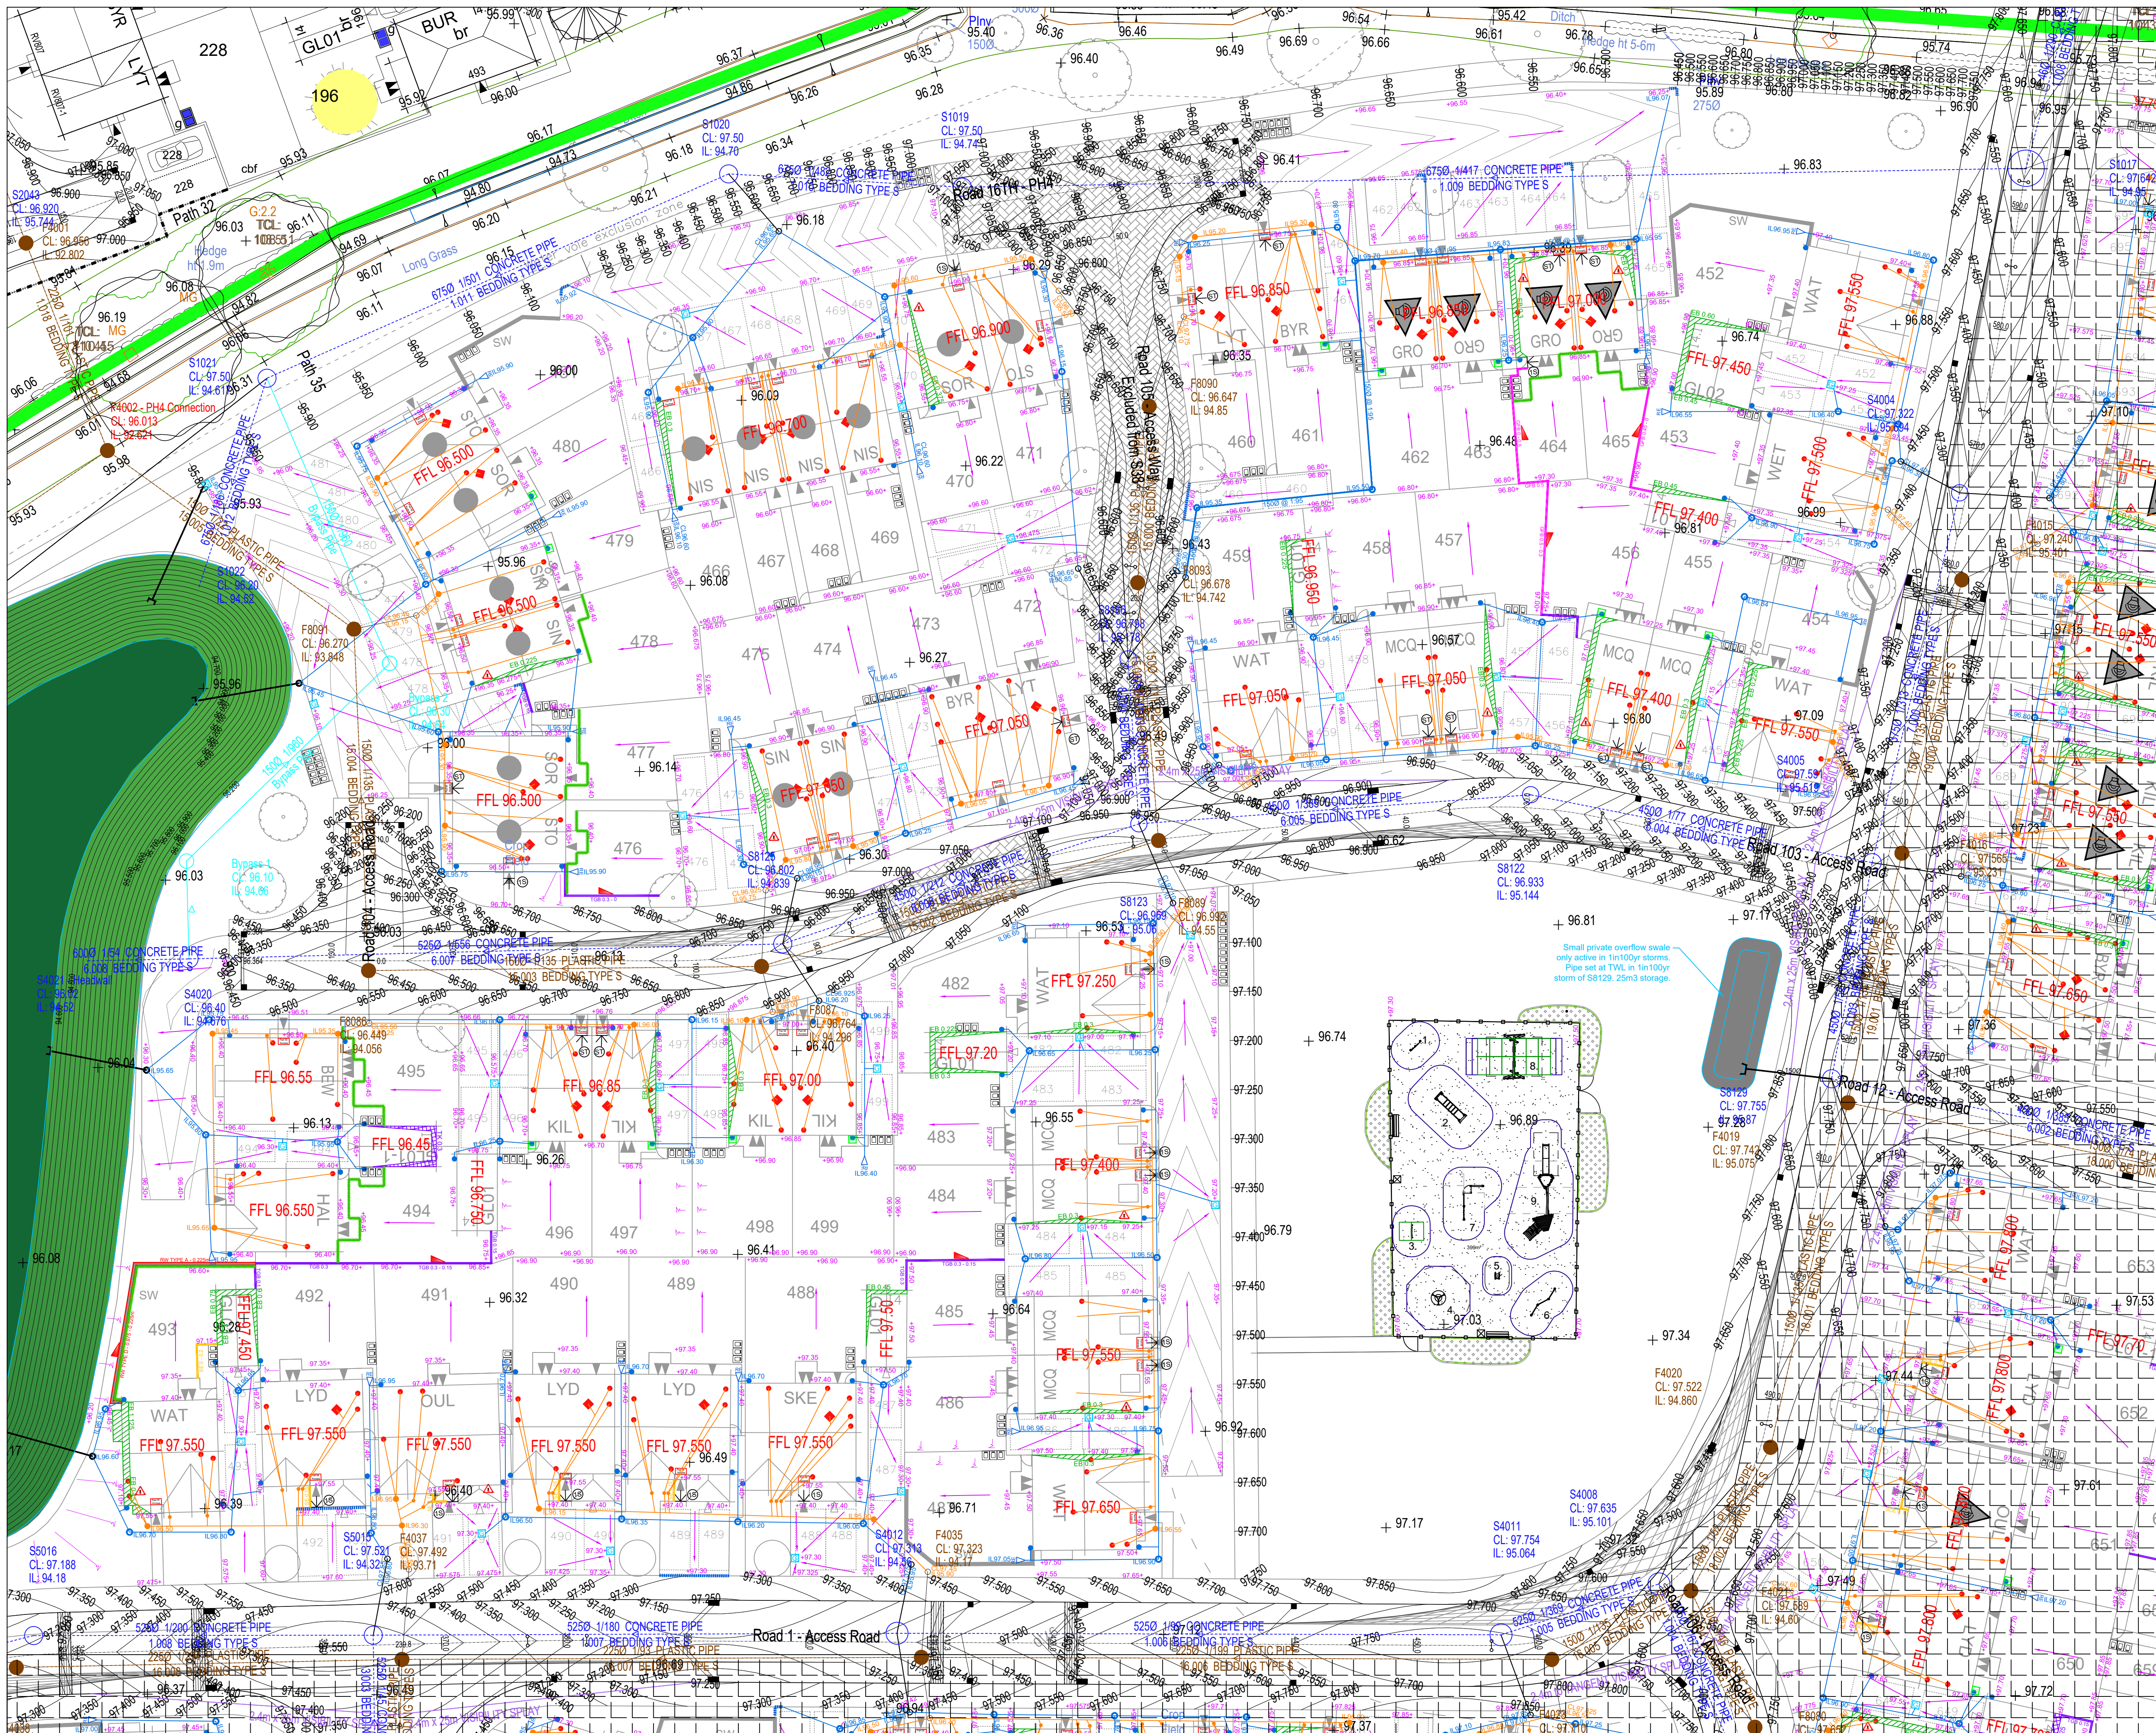

- KEY**
- FFL 141.40 Proposed plot Finished Floor Level
 - FFL 141.25 Proposed garage Slab Level
 - +141.95 Proposed external level
 - Exposed face brickwork height below FFL (check FFL shown against proposed external levels to confirm)
 - Tanking face brickwork retaining height above FFL (tanking face brickwork to be continued 0.15m above this given height)
 - Slab on Edge retaining structure (maximum retained height shown)
 - Timber Gravel Board retaining structure (maximum retained height shown)
 - GWB 0.3 Gravel Board retaining structure (maximum retained height shown)
 - GWB 0.6 Gravel Board with fence above & 10 foot concrete posts. (maximum retained height shown)
 - Brick retaining structure (type and maximum retained height shown)
 - Reinforced Concrete & brick retaining structure (type and maximum retained height shown)
 - Fall protection (600mm drop) (1.1m high metal vertical bar railings)
 - Wedge denotes stepping of brickwork for retaining walls & other retaining structures. i.e. GBF
 - Thick end = High end of retaining structure
 - Point end = Low end of retaining structure
 - Steps (300mm going; 150mm max rise) Number required indicated
 - Steps (300mm going; 200mm max rise) Number required indicated - in line with Building Regs Part K
 - Step at Threshold
 - Embankment works (max 1 in 3 gradient unless otherwise stated)
 - Garden or driveway fall direction arrow (high to low; arrow head indicates low)
 - Channel Drain
 - Gully with Cast Iron Grate
 - Private storm drain (invert level shown)
 - 450mm dia. private storm Universal Inspection Chamber
 - Sealed Rodding Eye
 - GARDEN DRAIN (indicated at retaining wall locations and where gardens fall towards the rear of plots to run to granular surround of nearest drainage) To be built to detail EM-50-003
 - Back Inlet Gully
 - Private foul drain (invert level shown)
 - 460mm dia. private foul Universal Inspection Chamber
 - Proposed bin storage location - bin store and path leading to it to be slabbed (path max 900mm wide)
 - Contractor to ensure meter positions sit 900-1200mm above finished ground level where under build is up to 750mm. If a situation occurs where meter positions exceed this, please report it to the Bloor Homes Engineer.
 - Denotes the plot's Part M access

NOTES

- All brickwork to be stepped in accordance with ground levels
- Lateral manholes to be 450mm plastic chambers
- Garden drains to be finished with stone, not turfed over
- All patios to have a fall on, either away from the house or towards to gravel strip
- FFLs may vary up to a tolerance of 375mm + or - the value stated on the drawing.

Revision:

Revision	Date	By
A	17.04.24	DS
B	31.05.24	DS
C	10.06.24	DS
D	11.07.24	DS
E	03.10.24	DS
F	06.12.24	DS
G	17.12.24	DS
H	03.01.25	DS
J	19.03.25	DS

Proposed Development at
**NORMANDY WAY
HINCKLEY**

**PHASE 4 - External
Works Plots 452-499**

DATE: 11.01.24
SCALE: 1:250 @ A1
DRAWN: DS
CHECKED: --

BLOOR HOMES

Drawing No. M100-EN-421J
